M. A. R. 57 (Rule 116)
Measurement Book

No. B 225043

Serial No. 2nd and Part Bill

Name of Work ..... From..... To.....

Name of Contractor of nature of Agency ..... KREDL (Work) Bangalore

Date of commencement of work ..... D.O. Release = 12/09/2018

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Name of work	Improvements to main and cross Roads at Babanna. Layout and Back roads area Chikkasandra in Ward No. 12. Shettyhally Sub-Division					
	Estimated cost Rs	= 50.40 Lks					
	JTB.No	= 012-1717-000036					
	Work order No	= EE/DD/200/157/17-18				Dt 22-9-2017	

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	(1) Excavation Excavation by manual means in hard soil in trenches for drainage pipes 2 m and above wide upto 0.90 m. Excavated surface leveled and sides neatly trimmed, the disposal earth to be levelled neatly either beside of trench complete as per specifications, lifts all leads and lifts including removing the excavated earth dirt, debris and over burden, earth are to be used as refilling disposal by using proper tickness this including the refilling leveling of where ever required complete as per specifications.						

M. A. R. 57 (Rule 116)
Measurement Book

No. B 225044

Serial No. .....
Name of Work ..... From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
	2	3	4	5	6	7	8
		Brought from M.B. p.no. 225084					
		Item no. (1) = 169.37 m³ + 208.82 m³					850 67.00
	(2) Providing and laying in position plain cement concrete 1:4:8 (1 cement 4 coarse sand 8 graded granite metal) using 40 mm and down size aggregate @ 0.85 m³ and fine aggregate @ 0.57 m³, mixing machine and manually laid in layers not exceeding 15 cms thick fully compacted in final, finishing curing, all						

Scanned by CamScanner

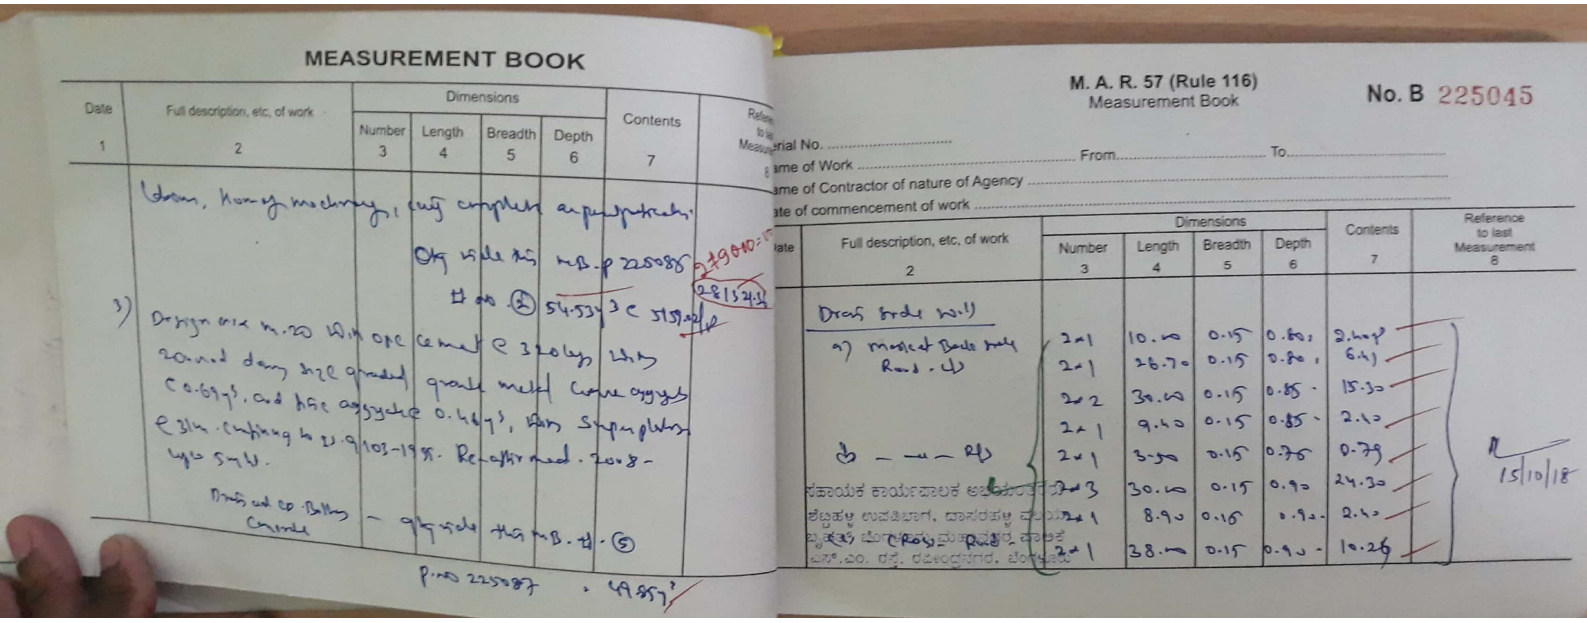

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Drain, Hume pipe laying, Earth excavation and backfilling						
	Page No. 225087						
	Total (5)					54.534	
3)	Design mix M.20 with OPC cement @ 320 kg/m³ using 20 mm down size graded granite metal, Coarse aggregate 0.69 m³, and fine aggregate 0.44 m³, using Superplasticizer @ 3 kg. cft/bag to 21.9/10% - 19%. Retaining wall. 2008 -						
	Drain and CD Building Concrete						
	Page No. 225087					49.854	

M. A. R. 57 (Rule 116)
Measurement Book

No. B 225045

Serial No. .....
Name of Work ..... From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
	2	3	4	5	6	7	8
	Drain brick wall						
	a) Market Bada main Road - (4)	2×1	10.00	0.15	0.80	2.40	
		2×1	26.70	0.15	0.80	6.41	
		2×2	34.00	0.15	0.85	15.30	
		2×1	9.40	0.15	0.85	2.40	
	(b) — " — (4)	2×1	3.50	0.15	0.75	0.79	
	ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ ಕಛೇರಿ	2×3	30.00	0.15	0.90	24.30	
	ಶೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ಪಟ್ಟಣ	2×1	8.90	0.15	0.90	2.40	
	ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ, ದಾಸರಹಳ್ಳಿ ವಲಯ, ಬಿ.ಎಸ್.ಎಂ. ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು	2×1	38.00	0.15	0.90	10.26	

15/10/18

Scanned by CamScanner

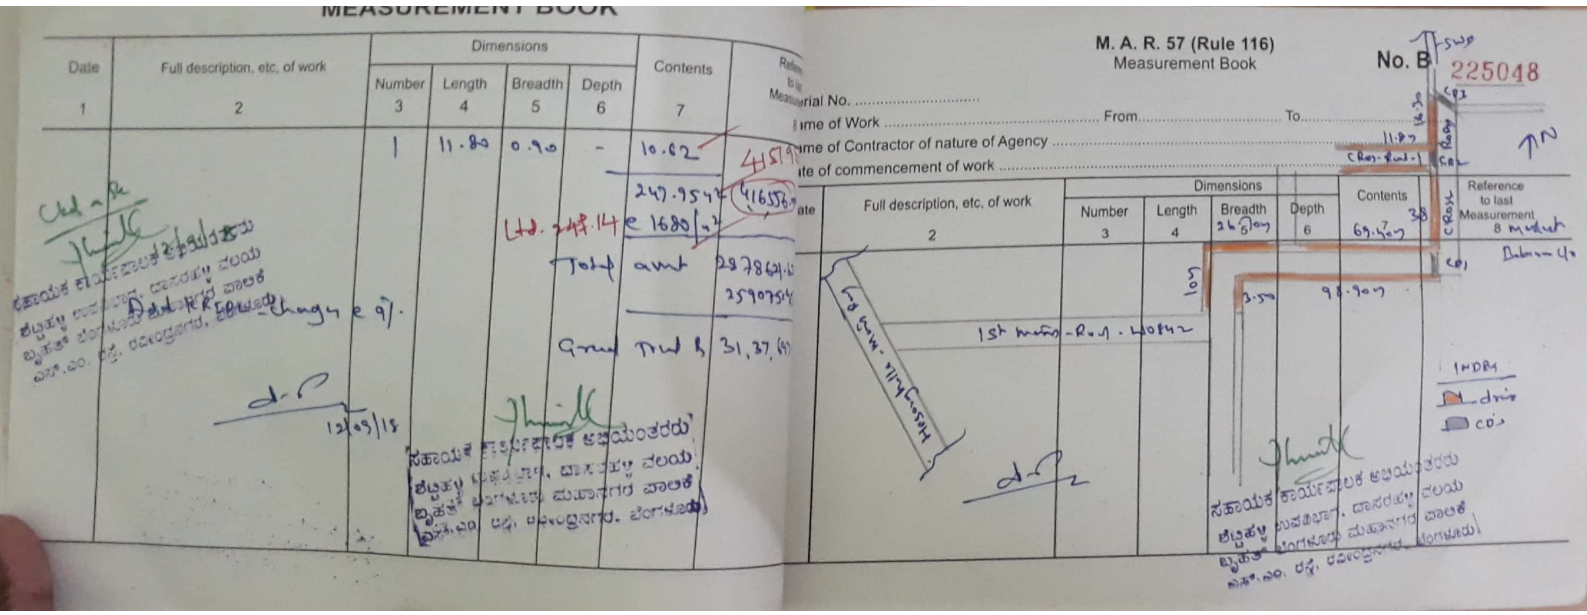

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
		1	11.80	0.90	-	10.62	
						247.954	
						Total amt	2878641.6
							2590754
						Grand Total Rs	31,37,695
12/09/18							

M. A. R. 57 (Rule 116)
Measurement Book

No. B 225048

Name of Work ..... From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
	2	3	4		6		8
			105	2.50		98.90	

1st main - R.C. - 40842

INDRA
drain
cols

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಕೆಬ್ಬಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಮಹಾ.ಎಂ. ರಸ್ತೆ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು

Scanned by CamScanner
